

## Bulletin # 04

11th February 2016

Construction works on the Stocklake Link Road (urban) Highway Improvement Scheme have now started in earnest. The contractor, North Midland Construction PLC is committed to delivering the works in a considerate manner and to the highest level of quality so that residents and businesses can benefit from the new Link Road and Service Road when completed. NMC will use locally recruited staff, employ an apprentice locally and work with Stocklake Park School on its local projects.

This bulletin will be the first of many to keep the local community up to date on how the scheme is progressing as well as on upcoming works.

### Summary of Works Ongoing

- NMC Site Compound and Offices are now set up, in front of Stocklake Park School.
- Earthworks to form the new link road have started, with the topsoil stripped (so that it can be re-used) ahead of the main excavation.
- Archaeology works.
- See the next page for section areas, with key construction dates.


### Summary of Works Upcoming (next few weeks)

- Section 3 will have plastic netting (geo-grid) and road stone placed to create the base for the new road.
- Installation of the new road drainage will begin shortly after this.
- The old Petrol Station will be coming down, with underground tanks being removed.
- The new Link Road is due for completion by the end of May 2016, with modification of the existing road complete around November 2016.

### Photo of the Week – Excavation within Section 3



### Stocklake Link Road – Plan showing Section

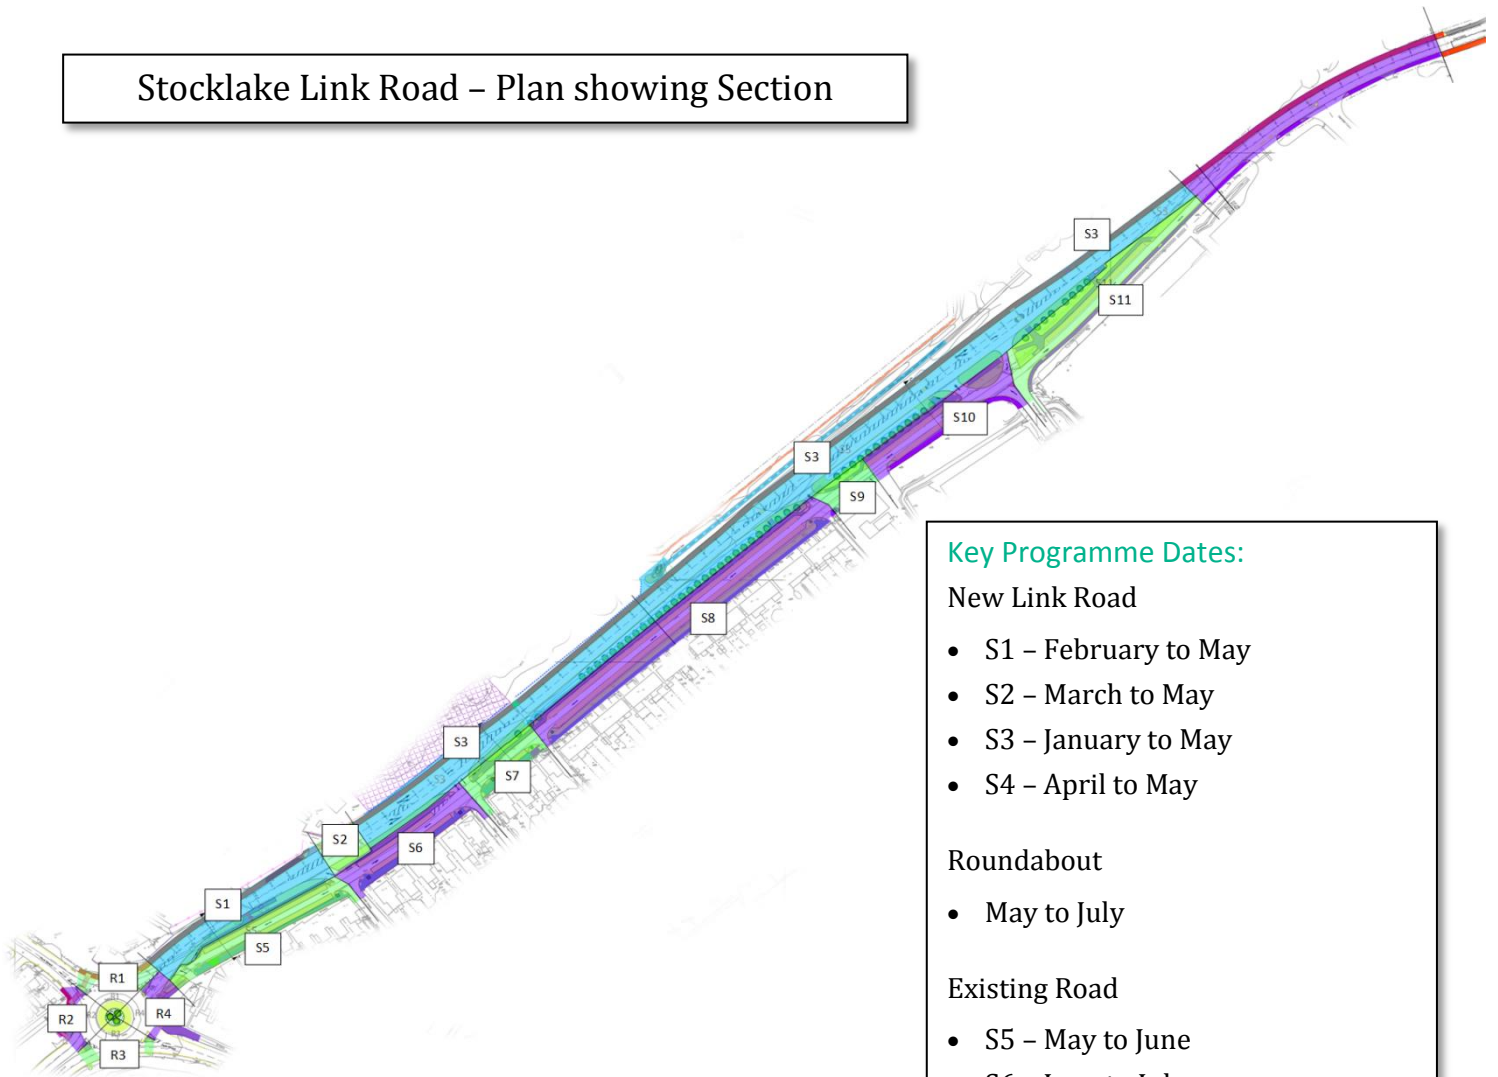

#### Key Programme Dates:

##### New Link Road

- S1 – February to May
- S2 – March to May
- S3 – January to May
- S4 – April to May

##### Roundabout

- May to July

##### Existing Road

- S5 – May to June
- S6 – June to July
- S7 – July
- S8 – July to August
- S9 – August
- S10 – August to September
- S11 – September
- Resurface existing road - September

NMC aim to keep disruption to an absolute minimum throughout the construction of these works; however, there will be a number of lorry movements required to deliver materials and take away excavated earth. Temporary traffic lights will be established and short-term diversions will be implemented – these will be advertised well in advance and diversion routes will be relatively short.



# Stocklake Link Road (urban) Highway Improvement Scheme

**Buckinghamshire**  
Thames Valley LOCAL ENTERPRISE  
PARTNERSHIP  
THE ENTREPRENEURIAL HEART OF BRITAIN

## Site Compound



## Site Emergency Contacts

In the event of an incident or emergency please contact;

**Site Agent Kane Kelly, North Midland Construction PLC – 07528 981850**

**Project Manager Akin Soetan, Buckinghamshire County Council – 01296 531395**

Please view our scheme webpages at <http://www.buckscc.gov.uk/aylesburyeast> . We will also be using Twitter **#aylesburyeast**

Please contact your local representative, Councillor Phil Gomm at [pgomm@buckscc.gov.uk](mailto:pgomm@buckscc.gov.uk) for more information about Stocklake Link Road and developments in the East of Aylesbury.

Thank you for your cooperation during the construction.

**Akin Soetan**  
Lead Project Officer  
Buckinghamshire County Council
